




Mary Rhodes Pipeline Phase 2



Council Presentation
June 20, 2017




Location Map

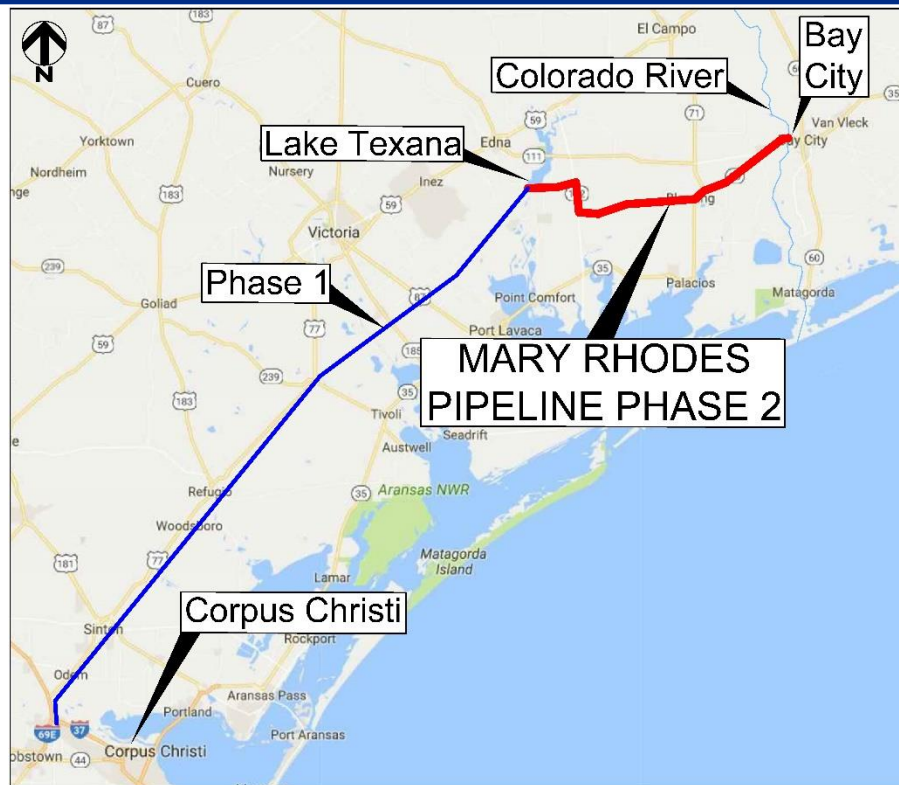



Location Map

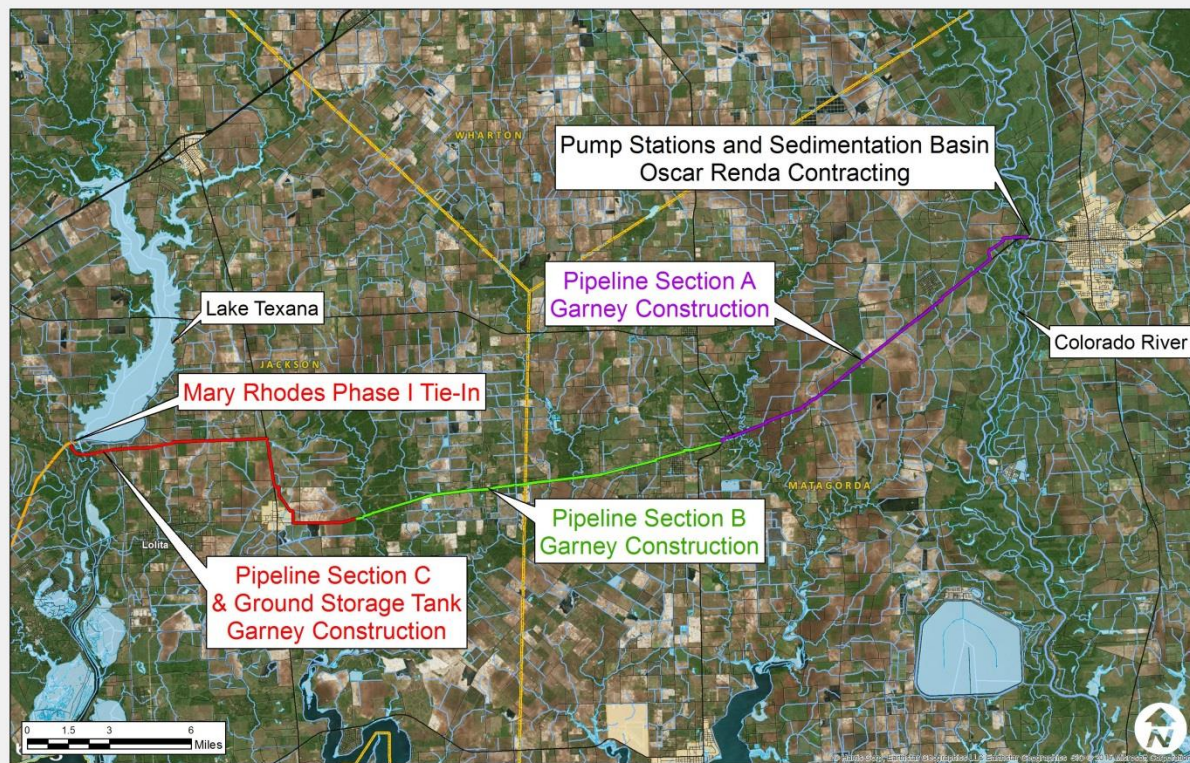



Project Status



Contract	Contractor	Contracted Start Date	Contracted Completion Date	Current Status
Pump Station / Sedimentation Basin	Oscar Renda Contracting	23-Apr-14	6-Aug-15	Substantially Complete September 2016
Pipeline Section A	Garney Companies, Inc.	17-Apr-14	16-Jun-15	Substantially Complete August 2015
Pipeline Section B				
Pipeline Section C				



Project Scope



Extended construction management services with Freese & Nichols, Inc. from March 2016 through completion of punch list correction that includes:

- ✓ On-going construction management for Pump Station/Sedimentation Basin punch list
- ✓ Technical support to the Ground Storage Tank
- ✓ Liquidated Damages negotiations with the Contractor
- ✓ Project close out services

Note: The construction contracts provide for liquidated damages (\$3,500/day). That will be evaluated against excusable and non-excusable (Contractor) delays as the project continues.



Project Schedule



2016										2017						
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
Construction Management Services																
