


# Flato Road Agnes to Bates

## Bond 2014 Proposition 2




Council Presentation  
September 13, 2016

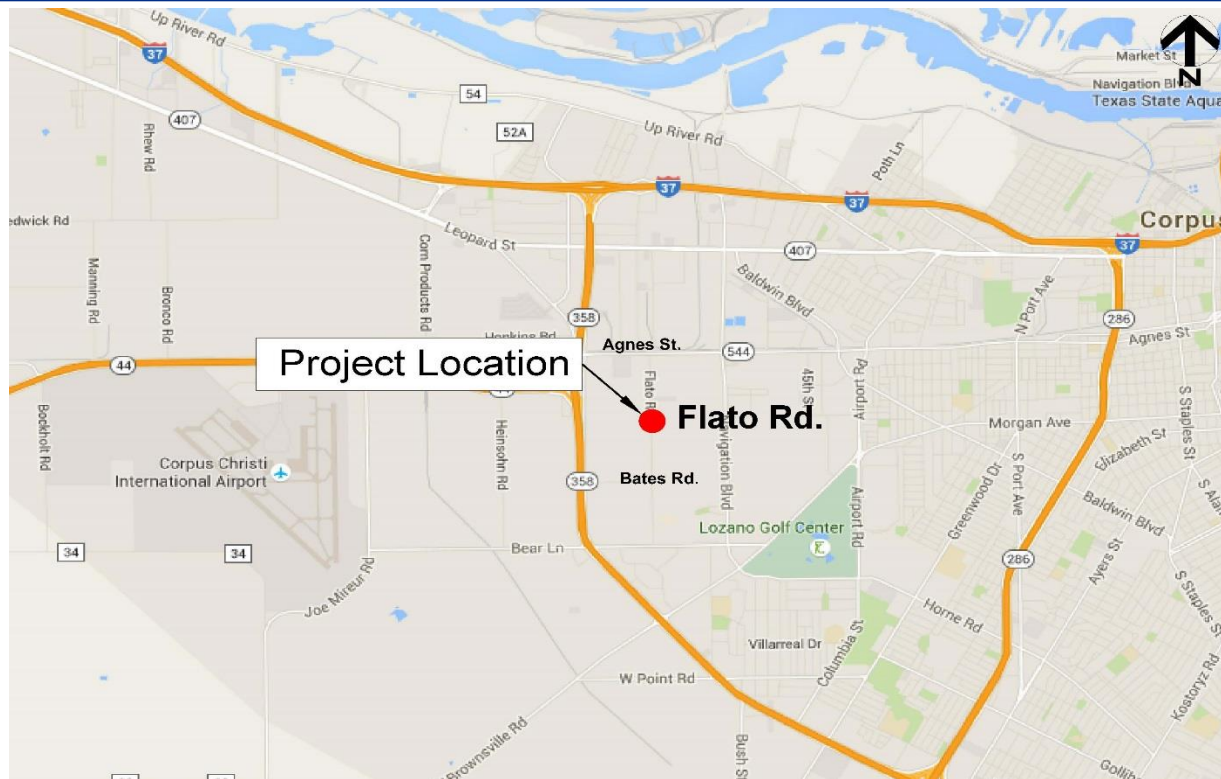



# Project Location

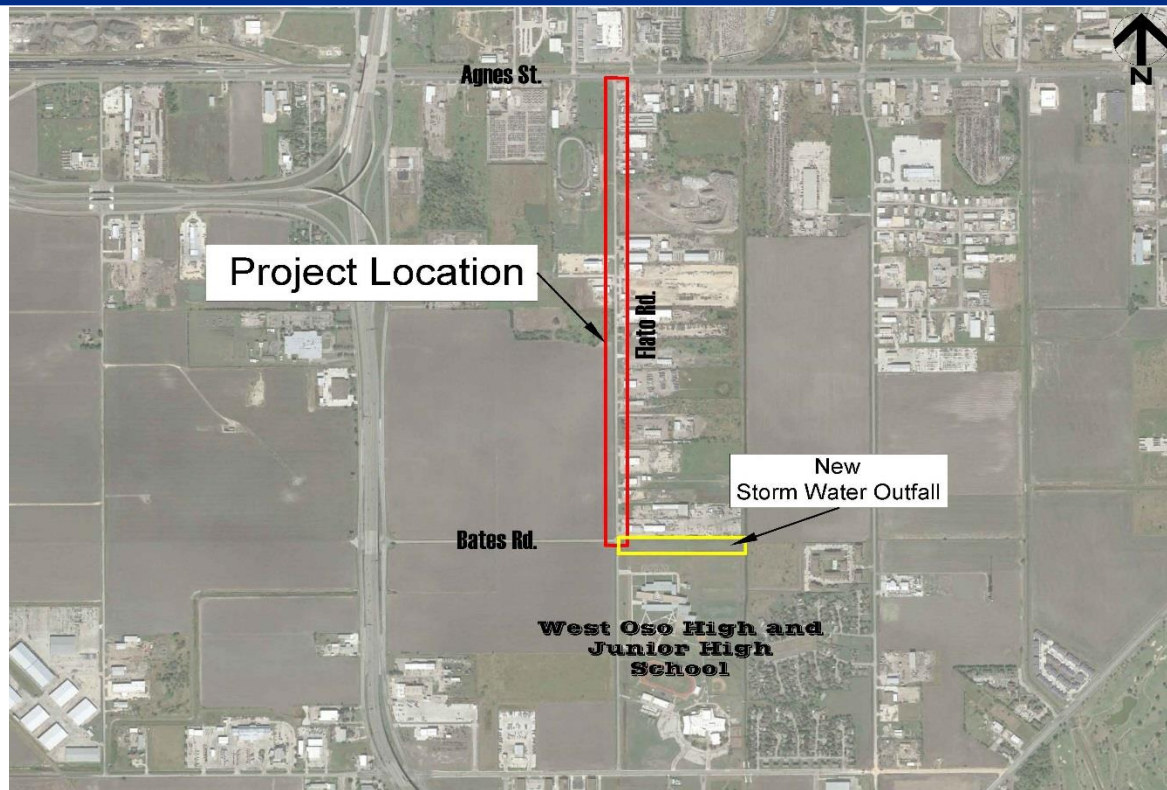



# Project Scope




Flato Road is an existing rural 22' road section with bar ditches and no curb & gutter or sidewalks. The following provides major work items:

- Full depth repair & restoration with slight widening of the existing 22' two-lane rural roadway
- New separated sidewalk for the developed (east side) of the roadway only.
- Utility improvements include water, wastewater and storm water.
  - ✓ New 8" water line
  - ✓ Wastewater line improvements
  - ✓ New underground drainage on the developed side with new area inlets
  - ✓ Re-grading the existing roadside ditch on the west undeveloped side
  - ✓ New 1,350 LF outfall channel from Flato Road to the Enterprize Channel to alleviate existing flooding along the roadway
- ❖ Future action includes land acquisition for drainage and other improvements



# Project Schedule



2015					2016							2017	
Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
Preliminary Design									Design				

**Bid Phase: Feb 2017 – May 2017**  
**Construction Phase: June 2017 – Aug 2018**
